

Dermaesthetic Super Apps - MVP Development Roadmap

Date: 2026-06-17 **Status:** Draft - Pending Approval **Approach:** Phased Parallel Streams (Approach C)
Deferred: Laundry, Loyalty & Membership

Executive Summary

Metric	Value
Total Features	14 (11 Phase 1 + 3 Phase 2)
Total Sprints	28 weeks (1 sprint = 1 week)
Buffer Weeks	4 weeks (strategic placement)
Team	2 Flutter devs, 2 Fullstack (CMS/BE)
Timeline	June 2026 → January 2027
CTO Target	Beat by ~5 months

Buffer Strategy

Buffer Placement Rationale:

Buffer	Week	Purpose
BUF-1	5	Auth integration testing, Bug fixes after critical auth flow
BUF-2	13	Booking integration testing, Payment flow validation
BUF-3	23	Phase 2 integration testing, Cross-feature validation
BUF-4	27	Final QA, Regression testing, App store prep validation

Buffer Usage Rules: 1. Buffer weeks are for **integration testing and bug fixes**, not new features 2. Buffer weeks can be used for **documentation and code reviews** 3. Buffer weeks can be used for **performance optimization** 4. Buffer weeks **cannot be used for scope expansion** 5. If no issues arise, buffer weeks can be used for **technical debt reduction**

Backend Buffer Weeks:

Buffer	Week	Purpose
B-BUF-1	9	Integration testing, Bug fixes, API documentation updates
B-BUF-2	10	Performance optimization, Security audit, Final API adjustments

Team Allocation

Role	Count	Responsibility
Flutter Developer 1	1	Mobile app (Android + iOS)
Flutter Developer 2	1	Mobile app (Android + iOS)
Fullstack Developer 1	1	Backend APIs + CMS
Fullstack Developer 2	1	Backend APIs + CMS

Critical Path: Mobile development (2 Flutter devs) **Parallel Work:** Backend APIs can be built 1-2 weeks ahead of mobile consumption

Epic Breakdown

Epic 1: Authentication & Onboarding

Priority: P0 (Critical Path) **Sprint:** 3-5

Story 1.1: Login

Task	Subtasks	Estimate
Login screen UI	Email input, Password input, Login button, Divider, Social logins	2 days
OTP verification	Phone input, OTP input (6 digit), Resend timer, Verification API	2 days
State management	Form validation, Loading states, Error handling	1 day

Story 1.2: Register

Task	Subtasks	Estimate
Register screen UI	Name, Email, Phone, Password, Confirm password, Register button	2 days
Phone verification	OTP send, OTP verify, Phone validation	1 day
Email verification	Email OTP, Verification flow	1 day
State management	Form validation, Loading, Error handling	1 day

Story 1.3: Forgot Password

Task	Subtasks	Estimate
Email input screen	Email input, Send reset link button	0.5 day
Reset password screen	New password, Confirm password, Submit	0.5 day
Success screen	Confirmation message, Back to login	0.5 day
API integration	Reset request, Password update	0.5 day

Story 1.4: Onboarding Tutorial

Task	Subtasks	Estimate
Tutorial screens	3-4 intro screens with illustrations	1 day
Navigation	Skip button, Next/Previous, Get Started	0.5 day
First-launch detection	Store flag in local storage	0.5 day

Epic 2: Homepage

Priority: P0 **Sprint:** 6-7

Story 2.1: Non-Login Homepage

Task	Subtasks	Estimate
Hero banner	Carousel/promo banner	1 day
Brand section	Brand cards horizontal scroll	1 day
Promotion section	Promotion cards	0.5 day
Bottom navigation	Login CTA, nav items	0.5 day

Story 2.2: Logged-In Homepage

Task	Subtasks	Estimate
Search bar	Search input with icon	0.5 day
Brand carousel	Brand cards horizontal scroll	1 day
Booking CTA	Quick booking button	0.5 day
Promotion section	Promotion cards	0.5 day
History preview	Recent booking history	1 day
Profile preview	User avatar, name	0.5 day

Story 2.3: Search

Task	Subtasks	Estimate
Search screen	Search input, Results grid	1 day
Search API	Query, Filter, Debounce	1 day
Search results	Brand cards, Treatment cards	1 day

Epic 3: Brand Pages

Priority: P0 **Sprint:** 8-9

Story 3.1: Brand Listing

Task	Subtasks	Estimate
Brand list screen	Grid/list view, Filter/Sort	1.5 days
Brand card component	Image, Name, Rating, Location	1 day
Brand API	List endpoint, Pagination, Filters	1 day
Pull-to-refresh	Refresh indicator, Reload data	0.5 day

Story 3.2: Brand Detail

Task	Subtasks	Estimate
Brand header	Logo, Name, Rating, Location, Description	1 day
Treatment list	Treatment cards with prices	1 day
Clinic list	Clinic cards with distance	1 day
Brand API	Detail endpoint, Related data	1 day

Story 3.3: Clinic Page

Task	Subtasks	Estimate
Clinic header	Name, Address, Map link	0.5 day
Clinic details	Operating hours, Contact	0.5 day
Available treatments	Treatment list for this clinic	1 day
Clinic API	Detail endpoint	0.5 day

Story 3.4: Treatment Page

Task	Subtasks	Estimate
Treatment header	Name, Image, Description	0.5 day
Treatment details	Duration, Price, Pre-care, Post-care	1 day
Book now CTA	Navigate to booking	0.5 day
Treatment API	Detail endpoint	0.5 day

Epic 4: Booking Clinic

Priority: P0 (Critical Path - Complex) **Sprint:** 10-12

Story 4.1: Clinic Selection

Task	Subtasks	Estimate
Clinic selector	Dropdown/modal for clinic choice	1 day
Clinic search	Search within brand	0.5 day
Clinic card	Selected clinic display	0.5 day

Story 4.2: Treatment Selection

Task	Subtasks	Estimate
Treatment list	Available treatments for clinic	1 day
Treatment selection	Select one or multiple	1 day
Price summary	Total price calculation	0.5 day

Story 4.3: Date & Time Picker

Task	Subtasks	Estimate
Calendar component	Month view, Date selection	1.5 days
Time slot picker	Available time slots	1 day
Availability API	Fetch available slots	1 day

Story 4.4: Booking Confirmation

Task	Subtasks	Estimate
Booking summary	Clinic, Treatment, Date, Time, Price	1 day
User confirmation	Confirm button, Terms checkbox	0.5 day
Booking API	Create booking endpoint	1 day

Story 4.5: Payment

Task	Subtasks	Estimate
Payment method selection	Doku integration	1 day
Payment processing	Payment API integration	1.5 days
Payment success	Receipt, Confirmation screen	1 day
Payment failure	Error handling, Retry	0.5 day

Story 4.6: Booking Status

Task	Subtasks	Estimate
Booking status screen	Pending, Confirmed, Completed, Cancelled	1 day
Status updates	Real-time status via polling/websocket	1 day

Epic 5: Profile Management

Priority: P1 **Sprint:** 13-14

Story 5.1: Profile Page

Task	Subtasks	Estimate
Profile header	Avatar, Name, Email, Phone	1 day
Profile menu	Settings options list	0.5 day
Profile API	Get/Update profile	0.5 day

Story 5.2: Edit Profile

Task	Subtasks	Estimate
Edit profile form	Name, Email, Phone inputs	1 day
Avatar upload	Camera/Gallery picker	1 day
Save changes	API update, Validation	0.5 day

Story 5.3: Address Management

Task	Subtasks	Estimate
Address list	Saved addresses	0.5 day
Add address	Form with fields	1 day
Edit address	Edit existing	0.5 day
Delete address	Confirmation, Remove	0.5 day
Address API	CRUD endpoints	1 day

Story 5.4: Change Phone

Task	Subtasks	Estimate
Current phone display	Masked phone number	0.5 day
New phone input	Phone input with country code	0.5 day
OTP verification	Verify new phone	1 day

Task	Subtasks	Estimate
Phone update API	Update endpoint	0.5 day

Story 5.5: Change Password

Task	Subtasks	Estimate
Current password	Password input	0.5 day
New password	Password input with strength indicator	0.5 day
Confirm password	Match validation	0.5 day
Password update API	Update endpoint	0.5 day

Story 5.6: Face ID

Task	Subtasks	Estimate
Face ID setup	Biometric permission	0.5 day
Face ID toggle	Enable/Disable setting	0.5 day
Face ID login	Biometric authentication	1 day
Platform integration	iOS Face ID, Android Biometric	1 day

Story 5.7: Privacy Settings

Task	Subtasks	Estimate
Privacy toggles	Data sharing, Marketing consent	0.5 day
Privacy API	Get/Update preferences	0.5 day

Story 5.8: Contact Support

Task	Subtasks	Estimate
Support form	Message input, Category	1 day
Submit support	API submission	0.5 day
Support history	Previous tickets	0.5 day

Epic 6: Notifications

Priority: P1 **Sprint:** 11

Story 6.1: Notification Center

Task	Subtasks	Estimate
Notification list	Grouped by date, Read/Unread	1 day
Notification detail	Full notification content	0.5 day
Mark as read	Tap to read, Mark all read	0.5 day
Notification API	List endpoint, Pagination	1 day

Story 6.2: Push Notifications

Task	Subtasks	Estimate
FCM setup	Firebase Cloud Messaging	1 day
Token registration	Device token storage	0.5 day
Notification handling	Background/Foreground handling	1 day
Deep linking	Navigate to relevant screen	0.5 day

Epic 7: Promotions

Priority: P1 **Sprint:** 9

Story 7.1: Promotion Listing

Task	Subtasks	Estimate
Promotion list	Grid view, Filter by category	1 day
Promotion card	Image, Title, Discount, Expiry	0.5 day
Promotion API	List endpoint, Filters	1 day
Pull-to-refresh	Refresh indicator	0.5 day

Story 7.2: Promotion Detail

Task	Subtasks	Estimate
Promotion detail	Full image, Terms, Conditions	1 day
Use promotion	Navigate to booking/shop	0.5 day
Share promotion	Share sheet	0.5 day

Epic 8: History

Priority: P1 **Sprint:** 14

Story 8.1: Booking History

Task	Subtasks	Estimate
History list	Past bookings, Status indicators	1 day
History filter	Date range, Status filter	0.5 day
History detail	Booking details, Receipt	1 day
History API	List endpoint, Pagination	1 day

Story 8.2: Rebook

Task	Subtasks	Estimate
Rebook button	Quick rebook from history	0.5 day
Pre-fill booking	Copy previous booking details	0.5 day

Epic 9: Skin Analysis

Priority: P1 **Sprint:** 14

Story 9.1: Skin Analysis Questionnaire

Task	Subtasks	Estimate
Questionnaire screen	Multiple choice questions	1.5 days
Progress indicator	Step counter, Progress bar	0.5 day
Question types	Single select, Multi select, Scale	1 day
Questionnaire API	Save responses, Get questions	1 day

Story 9.2: Skin Analysis Results

Task	Subtasks	Estimate
Results screen	Skin type, Recommendations	1 day
Product recommendations	Related products	0.5 day
Save results	Store analysis locally	0.5 day

Epic 10: Healthy Food

Priority: P2 (Phase 2) **Sprint:** 15-16

Story 10.1: Healthy Food Listing

Task	Subtasks	Estimate
Food listing	Grid view, Categories	1 day
Food card	Image, Name, Price, Rating	0.5 day
Food API	List endpoint, Filters	1 day
Category filter	Filter by food type	0.5 day

Story 10.2: Food Detail

Task	Subtasks	Estimate
Food detail	Image, Description, Nutrition	1 day
Add to cart	Quantity selector	0.5 day
Food API	Detail endpoint	0.5 day

Story 10.3: Food Cart

Task	Subtasks	Estimate
Cart screen	Items list, Total price	1 day
Quantity update	Increase/Decrease/Remove	0.5 day
Checkout	Delivery address, Payment	1 day
Cart API	CRUD endpoints	1 day

Story 10.4: Food Order

Task	Subtasks	Estimate
Order confirmation	Order summary	0.5 day
Order tracking	Status updates	1 day
Order history	Past orders	0.5 day
Order API	Create, Track, List endpoints	1 day

Epic 11: Shop

Priority: P2 (Phase 2) **Sprint:** 16-17

Story 11.1: Shop Listing

Task	Subtasks	Estimate
Product listing	Grid view, Categories	1 day

Task	Subtasks	Estimate
Product card	Image, Name, Price, Rating	0.5 day
Shop API	List endpoint, Filters	1 day
Search products	Search with filters	1 day

Story 11.2: Product Detail

Task	Subtasks	Estimate
Product detail	Images, Description, Specs	1 day
Add to cart	Quantity, Variants	0.5 day
Reviews	User reviews, Ratings	1 day
Product API	Detail endpoint	0.5 day

Story 11.3: Shop Cart

Task	Subtasks	Estimate
Cart screen	Items list, Total price	1 day
Quantity update	Increase/Decrease/Remove	0.5 day
Promo code	Apply discount code	0.5 day
Checkout	Address, Shipping (JNE), Payment (Doku)	1.5 days
Cart API	CRUD endpoints	1 day

Story 11.4: Shop Order

Task	Subtasks	Estimate
Order confirmation	Order summary, Receipt	0.5 day
Order tracking	Shipping status, JNE tracking	1 day
Order history	Past orders	0.5 day
Order API	Create, Track, List endpoints	1 day

Epic 12: Treatment Transaction

Priority: P2 (Phase 2) **Sprint:** 17

Story 12.1: Transaction List

Task	Subtasks	Estimate
Transaction list	All transactions, Status	1 day

Task	Subtasks	Estimate
Transaction filter	Date, Status, Type	0.5 day
Transaction API	List endpoint, Pagination	1 day

Story 12.2: Transaction Detail

Task	Subtasks	Estimate
Transaction detail	Full details, Receipt	1 day
Invoice download	PDF generation	1 day
Transaction API	Detail endpoint	0.5 day

Epic 13: Skin Journey

Priority: P2 (Phase 2) **Sprint:** 17-18

Story 13.1: Skin Journey Page

Task	Subtasks	Estimate
Journey timeline	Vertical timeline, Milestones	1.5 days
Milestone cards	Treatment dates, Progress	1 day
Journey API	Get journey data	1 day

Story 13.2: Progress Tracking

Task	Subtasks	Estimate
Progress chart	Before/After photos	1 day
Progress notes	User notes per milestone	0.5 day
Photo upload	Camera/Gallery	1 day
Progress API	Upload, Get endpoints	0.5 day

Backend API Breakdown

Sprint 0 (Weeks 1-2): Foundation

Week	Tasks
Week 1	Project setup, Auth APIs (Login, Register, OTP, Forgot Password), User model, Database schema
Week 2	Brand APIs (List, Detail), Booking APIs (Create, List, Status), Promotion APIs (List, Detail)

Sprint 1 (Weeks 3-4): Core APIs

Week	Tasks
Week 3	Notification APIs (List, Mark read), Profile APIs (Get, Update, Address CRUD), Search API
Week 4	Treatment APIs (List, Detail), Clinic APIs (List, Detail), Skin Analysis APIs (Save, Get)

Sprint 2 (Weeks 5-6): Phase 2 APIs

Week	Tasks
Week 5	Healthy Food APIs (List, Detail, Cart, Order), Shop APIs (List, Detail, Cart, Order)
Week 6	Treatment Transaction APIs (List, Detail), Skin Journey APIs (Get, Update), Integration testing

Sprint 3 (Weeks 7-8): CMS & Polish

Week	Tasks
Week 7	CMS dashboard (React/Next.js), Content management for promotions, brands
Week 8	API documentation, Performance optimization, Security audit

Buffer Sprints (Weeks 9-10): Integration & Security

Week	Tasks
Week 9	Integration testing, Bug fixes, API documentation updates
Week 10	Performance optimization, Security audit, Final API adjustments

Weekly Sprint Plan

Backend Sprints (Fullstack Devs)

Sprint	Week	Focus	Deliverables
B-1	1	Foundation	Project setup, Auth APIs, User model, DB schema
B-2	2	Core APIs	Brand, Booking, Promotion APIs
B-3	3	Extended APIs	Notification, Profile, Search APIs
B-4	4	Domain APIs	Treatment, Clinic, Skin Analysis APIs
B-5	5	Phase 2 APIs	Healthy Food, Shop APIs (Cart, Order)
B-6	6	Phase 2 APIs	Treatment Transaction, Skin Journey APIs
B-7	7	CMS	Dashboard, Content management


Sprint	Week	Focus	Deliverables
B-8	8	Polish	Documentation, Optimization, Security
B-BUF-1	9	Buffer	Integration testing, Bug fixes, API documentation
B-BUF-2	10	Buffer	Performance optimization, Security audit

Mobile Sprints (Flutter Devs)

Sprint	Week	Focus	Deliverables
M-1	3	Setup & Auth	Flutter project, Login screen, OTP verification
M-2	4	Auth Complete	Register, Forgot Password, Onboarding tutorial
BUF-1	5	Buffer	Auth integration testing, Bug fixes, Documentation
M-3	6	Homepage	Non-login homepage, Logged-in homepage
M-4	7	Homepage Complete	Search functionality, Brand carousel
M-5	8	Brands	Brand listing, Brand detail
M-6	9	Brands Complete	Clinic page, Treatment page
M-7	10	Booking (Part 1)	Clinic selection, Treatment selection, Date picker
M-8	11	Booking (Part 2)	Time picker, Booking confirmation, Payment
M-9	12	Booking Complete	Booking status, Push notifications
BUF-2	13	Buffer	Booking integration testing, Payment flow validation, Bug fixes
M-10	14	Profile	Profile page, Edit profile, Address management
M-11	15	Profile Complete	Change phone, Change password, Face ID, Privacy
M-12	16	Promotions	Promotion listing, Promotion detail
M-13	17	History & Skin	Booking history, Skin analysis questionnaire
M-14	18	Phase 2 Start	Healthy Food listing, Food detail, Food cart
M-15	19	Food Complete	Food order, Order tracking
M-16	20	Shop	Shop listing, Product detail, Shop cart
M-17	21	Shop Complete	Shop order, Order tracking
M-18	22	Treatment & Journey	Treatment transaction, Skin journey
BUF-3	23	Buffer	Phase 2 integration testing, Cross-feature validation, Bug fixes
M-19	24	Polish (Part 1)	UI polish, Animation, Performance
M-20	25	Polish (Part 2)	Bug fixes, Edge cases, Accessibility

Sprint	Week	Focus	Deliverables
M-21	26	QA & Testing	Integration testing, E2E testing
BUF-4	27	Buffer	Final QA, Regression testing, App store prep validation
M-22	28	Store Prep	App store assets, Submission, Release

Gantt Chart

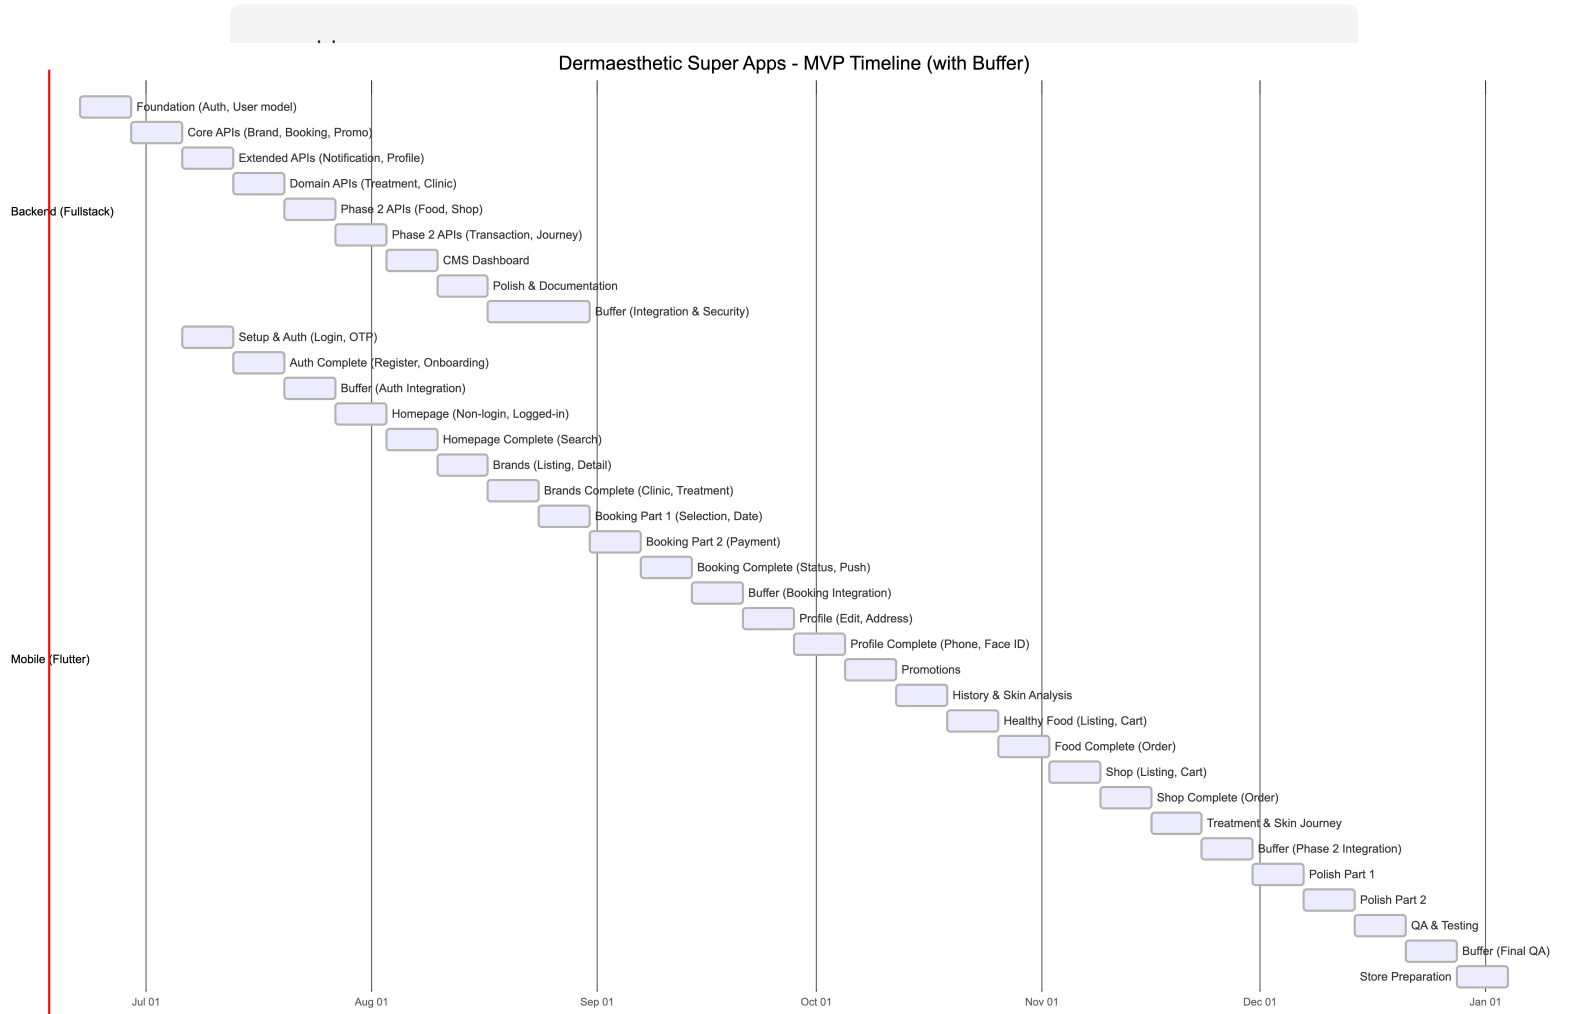


Risk Register

Risk	Impact	Mitigation
Flutter dev bottleneck	High	Backend APIs ready 1-2 weeks ahead, parallel development

Risk	Impact	Mitigation
Doku payment integration issues	Medium	Early integration testing, Fallback payment method
JNE delivery integration issues	Medium	Early API testing, Mock for development
App store rejection	Medium	Follow guidelines, Pre-submission review
Scope creep	High	Strict MVP scope, Deferred features documented
Team burnout	Medium	Realistic sprint loads, Buffer weeks included
Buffer week misuse	Medium	Buffer weeks are for integration testing and bug fixes, not new features
Integration issues	High	Buffer weeks placed after critical features (Auth, Booking, Phase 2)
Timeline slippage	Medium	4 buffer weeks provide 17% schedule flexibility
Backend delays	Medium	Backend has 2 buffer weeks for integration and security testing

Dependencies

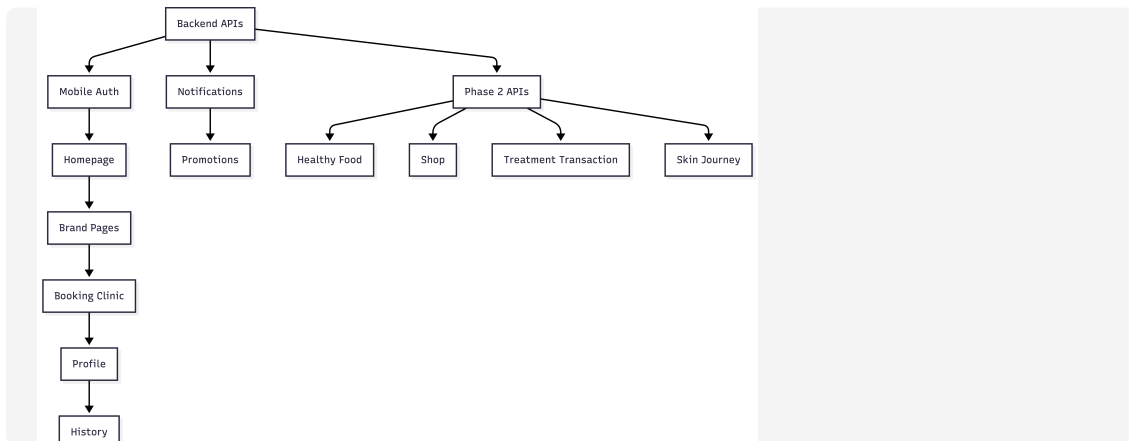

Approval Checklist

- ☐ Epic breakdown approved
- ☐ Sprint plan approved
- ☐ Gantt chart approved
- ☐ Risk register reviewed
- ☐ Dependencies validated
- ☐ Deferred features confirmed (Laundry, Loyalty)
- ☐ Timeline accepted (28 weeks mobile with 4 buffer weeks, 10 weeks backend with 2 buffer weeks)
- ☐ Buffer week placement approved
- ☐ Buffer usage rules approved
- ☐ Backend buffer weeks approved (Weeks 9-10 for integration and security)
